Project: Smart Parking Platform

Version: 7.1

Date: 10.29.2026

Table of Contents

1. Software Requirements Specification (SRS) 2
1.1 Introduction 2
1.11 Purpose 2
1.12 Scope 3
1.2 Overall Description 3
1.21 Users: 3
1.22 System Environment: 3
1.23 Constraints: 3
1.24 Assumptions: 4
1.3 Functional Requirements 4
1.4 Non-Functional Requirements 4
1.5 Use Cases 5
Use Case 1 5
3.1 Gantt Chart 8
3.2 Milestones 9
4.1 Login 9
4.2 User/Operator UI 9
4.3 User/Operator Backend 10
4.4 Reporting Frontend/Backend 12
4.5 Trello Board 13
5. Risk Management 13
5.1 Technical Risks 13
5.2 Schedule Risks 14
5.3 Financial Risks 14
5.4 People Risks 14
5.5 Risk Assessment Standards 15
5.51 Probability Scale 15
5.52 Impact Scale 15
5.53 Risk Matrix 15
5.6 Risk Response Strategies 16
5.7 Risk Register 16
6. Quality Management 17
6.1 Quality Assurance 17

6.2 Quality Control 17
6.3 Quality Metrics 18
7. Communication Management Plan 18
7.1 Meeting Cadence 18
7.2 Reporting Methods 19
7.3 Communication Tools 19
8. Resource Management Plan 19
8.1 Project Resource Plan 19
9. RACI Matrix 20
10. Cost Management Plan 21
10.1 Labor Cost Estimate 21
10.2 Non-Labor Costs 21
10.3 Project Budget Summary 22
10.4 CAPEX vs OPEX 22
10.5 Monthly Cashflow 22
10.6 Hidden Costs and Mitigation 22
10.7 Earned Value Management (EVM) 23
11. Stakeholder Management 24
11.1 Stakeholder Analysis 24
11.2 Power–Interest Grid 24
12. Project Charter 24
13. Team Charter 25
13.1 Team Roles 25
13.2 Team Standards 25
13.3 Leadership and Conflict Resolution 26

1. Software Requirements Specification (SRS)

1.1 Introduction

1.11 Purpose

This document defines the initial requirements for the Smart Parking Platform developed by WE ARE $oftware ¢orp. The system will help drivers locate, reserve, and pay for parking spaces in real time while providing parking operators with tools to manage their facilities and monitor occupancy. The platform will be available through web and mobile applications and will provide parking availability information, navigation assistance, and management tools for parking operators. The goal is to develop a project management plan for the creation of this system, including requirements gathering, stakeholder management, scheduling, budgeting, risk management, and team coordination.

1.12 Scope

The project will provide web and mobile applications that support parking searches, real-time availability, reservations, digital payments, navigation, notifications, and parking management. The project will also provide an administrative dashboard for parking operators to manage facilities and view occupancy information and reports. Physical parking garage construction, manufacturing parking hardware, and direct control of city traffic systems are out of scope.

1.2 Overall Description

1.21 Users:

- Vehicle Owners
- Parking Facility Owners/Employees
- Finance and Billing Employees
- Third-Party Payment Providers
- City Transportation Employees
- Mobile Phone Users

1.22 System Environment:

The Smart Parking Platform will consist of web-based and mobile applications connected to backend/API services and a database. The system will also integrate with external mapping/navigation and payment services.

1.23 Constraints:

- The project has a fixed semester timeline.
- The project has an unlimited theoretical development budget.
- The system depends on third-party mapping, navigation, payment, and other APIs.
- The system must follow applicable security and privacy requirements.
- The system must consider applicable city ordinances and laws.
- Users must authenticate to access protected account and management functions.

1.24 Assumptions:

- Users have internet access.
- Users have a compatible web browser or mobile device.
- Parking facilities provide accurate availability and occupancy information.
- Third-party mapping and payment services are available when required.
- Parking operators will provide and maintain accurate facility information.

1.3 Functional Requirements

FR1: The system shall allow users to register and log in securely.

FR2: The system shall allow users to search for available parking locations.

FR3: The system shall display parking locations and availability on an interactive map.

FR4: The system shall allow users to reserve available parking spaces.

FR5: The system shall process digital parking payments through a supported payment provider.

FR6: The system shall provide users with reservation history and receipts.

FR7: The system shall send users reservation-related notifications and alerts.

FR8: The system shall provide navigation assistance to selected parking facilities through an external mapping service.

FR9: The system shall allow parking operators to add and manage parking facilities.

FR10: The system shall allow parking operators to monitor parking occupancy.

FR11: The system shall provide occupancy and parking usage reports.

FR12: The system shall allow authorized users to manage relevant account and parking information.

Additional functional requirements will be identified through stakeholder analysis and requirements elicitation throughout the semester.

1.4 Non-Functional Requirements

NFR1: The system shall support at least 1,000 concurrent users.

NFR2: The system shall display parking availability updates within 1 second when current data is available.

NFR3: The system shall target 99.99% uptime for critical services.

NFR4: The system shall protect user account, vehicle, reservation, and payment-related information.

NFR5: The system shall support modern web browsers and supported mobile devices.

NFR6: The system shall be scalable to support additional users and parking facilities.

NFR7: The system shall maintain consistent reservation and payment information when transactions are completed successfully.

1.5 Use Cases

Use Case 1

Title: Reserve a Parking Space

Actor: Driver

Precondition: User is logged in and a parking facility has an available space.

Steps:

- User searches for a parking location.

- User selects an available parking facility.
- User selects the reservation date and time.
- System verifies parking availability.
- User confirms the reservation and completes payment.
- System displays the reservation confirmation.

Postcondition: The parking reservation is saved to the user's account.

2. Work Breakdown Structure (WBS)

1. Smart Parking Platform
    1.1 User & Account Management
        1.1.1 User Registration & Login
            Account creation
            Secure login
        1.1.2 User Profile
            Account information
            Vehicle information
        1.1.3 Authentication & Security
            Authentication controls
            Protected user data
    1.2 Parking Search & Availability
        1.2.1 Parking Location Search
            Search available facilities
            Filter parking locations
        1.2.2 Real-Time Availability
            Display available spaces
            Update occupancy information
        1.2.3 Interactive Parking Map
            Display parking locations
            Select parking facility
    1.3 Reservations
        1.3.1 Space Selection
            Select parking facility
            Select available space
        1.3.2 Reservation Management
            Select date and time
            Confirm reservation
        1.3.3 Reservation History
            View past reservations
            View reservation details

- 1.4 Payments
  - 1.4.1 Payment Processing
    - Connect payment provider
    - Process parking payment
  - 1.4.2 Payment Confirmation
    - Confirm successful payment
    - Store transaction information
  - 1.4.3 Receipts
    - Generate digital receipt
    - View receipt history
- 1.5 Navigation & Notifications
  - 1.5.1 Navigation Integration
    - Connect mapping service
    - Provide directions to facility
  - 1.5.2 User Notifications
    - Reservation confirmation
    - Reservation alerts
- 1.6 Parking Operator Management
  - 1.6.1 Facility Management
    - Add parking facility
    - Update facility information
    - Remove facility
  - 1.6.2 Occupancy Management
    - Monitor occupancy
    - Update availability
  - 1.6.3 Operator Dashboard
    - View facility information
    - View parking activity
- 1.7 Reporting & Analytics
  - 1.7.1 Occupancy Reports
    - Generate occupancy reports
    - View occupancy trends
  - 1.7.2 Parking Usage Reports
    - Analyze parking usage
    - Review reservation activity
- 1.8 Testing & Deployment
  - 1.8.1 System Testing
    - Functional testing
    - Integration testing
  - 1.8.2 Security & Performance Testing
    - Security testing

Performance testing

1.8.3 Deployment

Deploy web application

Deploy mobile application


Deploy backend services

3. Project Timeline

WBS Component	Story Points	Risk
1.1 User & Account Mgmt	8	Moderate complexity; relies on secure auth standards
1.2 Parking Search & Availability	5	Depends on third-party map API reliability
1.3 Reservations	13	High complexity; requires state management & concurrency handling
1.4 Payments	8	Standard gateway integration but needs error/retry logic
1.5 Navigation & Notifications	3	Lightweight API calls; mostly configuration-driven
1.6 Operator Management	5	CRUD-heavy but straightforward UI/backend mapping
1.7 Reporting & Analytics	8	Requires data aggregation & charting libraries
1.8 Testing & Deployment	5	Cross-team coordination; environment setup overhead

WBS Component	Start	End	Duration	Dependencies
1.1 User & Account Mgmt	Sept Week 1	Oct Week 1	~5 wks	–
1.2 Parking Search & Availability	Sept Week 2	Oct Week 2	~5 wks	–
1.3 Reservations	Oct Week 1	Nov Week 1	~5 wks	1.2 (Finished)
1.4 Payments	Sept Week 4	Oct Week 3	~5 wks	1.4 (Started)
1.5 Navigation & Notifications	Oct Week 2	Nov Week 1	~5 wks	1.3 (Started)
1.6 Operator Management	Oct Week 3	Nov Week 2	~4 wks	1.3 (Finished) 1.4 (Started)
1.7 Reporting & Analytics	Nov Week 1	Nov Week 3	~3 wks	Backend API Calling
1.8 Testing & Deployment	Nov Week 2	Dec Week 2	~5 wks	First working Dev component required to start testing

3.1 Gantt Chart

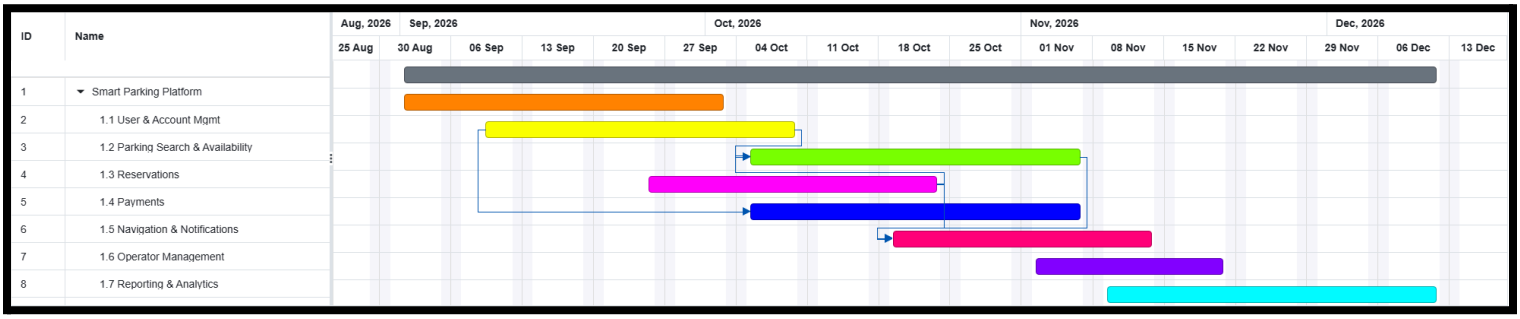

3.2 Milestones

Milestone	Target Date	Success Criteria
Requirements & WBS Baseline	Sept 7 (Week 1)	SRS v1.0 approved, WBS signed off by team leads
Sprint 1: Core Search & Auth Complete	Oct 9 (Week 6)	Users can log in, search lots, view live availability
Sprint 2: Reservation & Payment Flow Live	Nov 6 (Week 10)	End-to-end booking + payment confirmation working
Sprint 3: Operator Dashboard & Reports Ready	Nov 27 (Week 13)	Facilities manageable, occupancy/reports viewable
Sprint 4: Final Testing and Product Release	Dec 11th (Week 15)	Product Testing Completed, Product Released to public and team reorganized to focus on maintenance

4. Product Backlog

4.1 Login

ID	Task	Sprint #
1	User Registration	Sprint 1
2	User Login	Sprint 1

3	Secure Password Handling	Sprint 1
4	User Logout	Sprint 1
5	Role-based Access for Users and Operators	Sprint 1
6	Authentication Testing	Sprint 1
7	Password Reset	Sprint 2

4.2 User/Operator UI

ID	Task	Sprint #
1	User Registration Screen	Sprint 1
2	User Login Screen	Sprint 1
3	User Dashboard	Sprint 1
4	User Profile Screen	Sprint 1
5	Operator Dashboard	Sprint 1
6	Vehicle Information Screen	Sprint 2
7	Parking Search Screen	Sprint 2
8	Interactive Parking Map	Sprint 2
9	Parking Availability Display	Sprint 2
10	Parking Facility Details	Sprint 2
11	Operator Facility Management Screen	Sprint 2
12	Parking Reservation Screen	Sprint 3
13	Payment Screen	Sprint 3
14	Reservation Confirmation Screen	Sprint 3
15	Reservation Confirmation Notification	Sprint 3
16	Upcoming Reservation Reminder	Sprint 4
17	Reservation Cancellation Notification	Sprint 4
18	Reservation History Screen	Sprint 4

19	Payment History Screen	Sprint 4
20	Digital Receipt History Screen	Sprint 4

4.3 User/Operator Backend


ID	Task	Sprint #
1	User Account API	Sprint 1
2	Authentication API	Sprint 1
3	User Profile API	Sprint 1
4	Vehicle Information API	Sprint 2
5	Parking Facility API	Sprint 2
6	Parking Search API	Sprint 2
7	Real-time Availability API	Sprint 2
8	Occupancy Update API	Sprint 2
9	Operator Facility Management API	Sprint 2
10	Update Parking Facility Information	Sprint 2
11	Remove Parking Facility	Sprint 2
12	Update Parking Space Availability	Sprint 2
13	Integrate External Mapping Service	Sprint 2
14	Secure API Access and Authorization	Sprint 2
15	Reservation API	Sprint 3
16	Reservation Availability Validation	Sprint 3
17	Reservation Cancellation API	Sprint 3
18	Payment Processing Integration	Sprint 3
19	Payment Confirmation Processing	Sprint 3
20	Prevent Double Booking of Parking Spaces	Sprint 3
21	Handle Failed Payment Transactions	Sprint 3

22	Operator Occupancy Monitoring	Sprint 3
23	Provide Navigation to Selected Parking Facility	Sprint 3
24	Receipt Generation Service	Sprint 4
25	Reservation Cancellation and Refund Processing	Sprint 4
26	Record account and System Activity Logs	Sprint 4
27	Payment Integration Testing	Sprint 4
28	Final System Integration Testing	Sprint 5

4.4 Reporting Frontend/Backend

ID	Task	Sprint #
1	Reservation History	Sprint 3
2	Payment History	Sprint 3
3	Occupancy Report	Sprint 4
4	Daily Occupancy Report	Sprint 4
5	Weekly Occupancy Report	Sprint 4
6	Parking Usage Report	Sprint 4
7	Reservation Activity Report	Sprint 4
8	Facility Utilization Report	Sprint 5
9	Revenue/Payment Report	Sprint 5
10	Performance Testing for Concurrent Users	Sprint 5

4.5 Trello Board

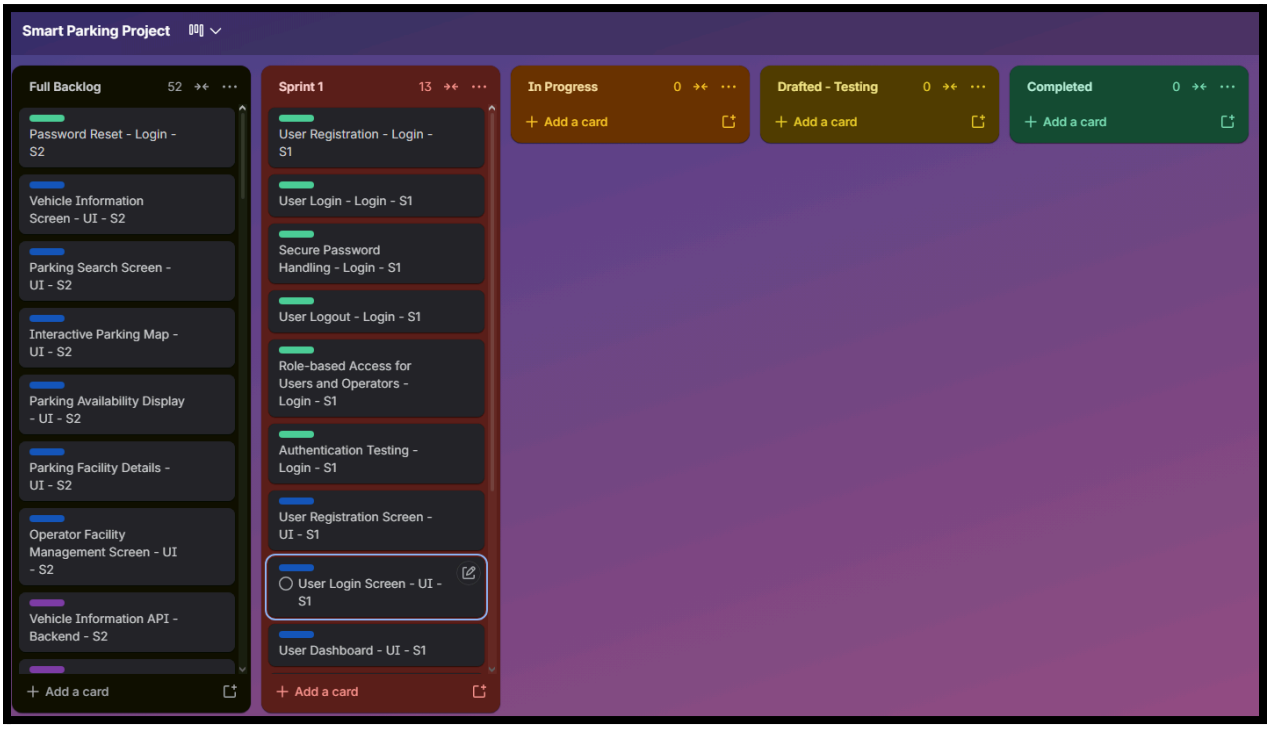

https://trello.com/invite/b/6ab5f184a1a2cb8fbdc54f2f/ATTI5ea9c23d87646c071dbde30ad65b95320CEA08EE/smart-parking-project

5. Risk Management

Risk management is important to the Smart Parking Platform because the project depends on real-time parking information, third-party services, multiple development teams, and a fixed semester timeline. Risks will be identified, assessed, monitored, and addressed throughout the project.

5.1 Technical Risks

ID	Risk Description
T1	Third-party mapping or navigation service becomes unavailable.
T2	Payment processing service experiences an outage or integration problem.

T3	Real-time parking availability information is inaccurate or delayed.
T4	Web and mobile applications have compatibility problems.

5.2 Schedule Risks

ID	Risk Description
S1	Requirements changes increase development time.
S2	Reservation functionality takes longer than planned.
S3	Third-party API dependencies delay development.
S4	Testing identifies defects that require additional development time.

5.3 Financial Risks

ID	Risk Description
F1	Third-party service fees change during the project.
F2	Payment provider fees are higher than expected.
F3	Additional security or compliance requirements create costs.
F4	Additional software or service subscriptions are needed.

- The project has an unlimited theoretical budget, but these risks are still tracked because outside services and project decisions may affect resource planning.

5.4 People Risks

ID	Risk Description
P1	A team member becomes unavailable during development.
P2	A development team lacks experience with a required technology or service.
P3	Communication problems occur between development teams.
P4	Stakeholder availability limits requirements feedback or approvals.

5.5 Risk Assessment Standards

5.51 Probability Scale

Value	Probability
5	Very High (>80%)
4	High (61–80%)
3	Moderate (41–60%)
2	Low (21–40%)
1	Very Low (<20%)

5.52 Impact Scale

Value	Impact
5	Catastrophic
4	Major
3	Moderate
2	Minor
1	Negligible

5.53 Risk Matrix

Probability \ Impact	1	2	3	4	5
5 Very High	Medium	High	High	Extreme	Extreme
4 High	Low	Medium	High	High	Extreme
3 Moderate	Low	Medium	Medium	High	High
2 Low	Low	Low	Medium	Medium	High
1 Very Low	Low	Low	Low	Medium	Medium

5.6 Risk Response Strategies

- Avoid: Change the project plan to eliminate a risk when possible.
- Mitigate: Reduce the likelihood or impact through actions such as testing, early integration, and backup plans.
- Transfer: Shift part of a risk to a third-party provider, such as a payment or mapping service.
- Accept: Monitor a risk when its impact is limited or prevention is not practical.

5.7 Risk Register

ID	Risk	Category	Probability	Impact	Level	Owner	Response
R1	Mapping service outage	Technical	4	4	High	Mapping Team	Mitigate
R2	Payment service failure	Technical	3	5	High	Payment Team	Mitigate
R3	Inaccurate parking availability	Technical	4	4	High	Backend Team	Mitigate
R4	Web/mobile compatibility issues	Technical	3	3	Medium	Mobile/Web Teams	Mitigate
R5	Requirements changes delay development	Schedule	3	4	High	Project Manager	Mitigate
R6	Reservation development delay	Schedule	4	4	High	Backend Team	Mitigate
R7	Third-party API delays	Schedule	3	4	High	Project Manager	Mitigate
R8	Testing requires major rework	Schedule	3	4	High	QA Team	Mitigate
R9	Third-party service fees increase	Financial	2	3	Medium	Project Manager	Accept
R10	Payment provider fees increase	Financial	2	3	Medium	Finance Team	Accept

R11	Additional security/compliance costs	Financial	2	4	Medium	Security Team	Mitigate
R12	Additional software subscriptions required	Financial	2	2	Low	Project Manager	Accept
R13	Team member becomes unavailable	People	3	4	High	Project Manager	Mitigate
R14	Technology skill gap	People	3	3	Medium	Team Lead	Mitigate
R15	Poor communication between teams	People	4	4	High	Project Manager	Mitigate
R16	Limited stakeholder availability	People	3	4	High	Project Manager	Mitigate

6. Quality Management

6.1 Quality Assurance

- Requirements reviews
- Design reviews
- Coding standards
- Peer code reviews
- Security reviews
- Sprint retrospectives

6.2 Quality Control

- Unit testing
- Integration testing
- System testing
- User acceptance testing
- Security testing

- Performance testing
- Regression testing
- Web and mobile compatibility testing

6.3 Quality Metrics

Metric	Target
System Availability	99.99%
Concurrent Users	1,000+
Availability Refresh	Less than 1 second
Critical Defects Before Release	0
Payment Processing Success	99%+
Reservation Accuracy	99%+

7. Communication Management Plan

Communication will coordinate the Mobile Application, Web Application, Backend/API, Mapping & Location Services, Payment Integration, and Quality Assurance teams while keeping project stakeholders informed.

7.1 Meeting Cadence

Meeting	Frequency	Participants	Purpose
Daily Stand-Up	Daily	Development teams, Project Manager	Progress and blockers
Team Review	Weekly	Team leads, Project Manager	Progress, risks, and dependencies
Sprint Review	Bi-Weekly	Project team, stakeholders	Demonstrate completed work
Stakeholder Meeting	Monthly	Project stakeholders	Project status and major decisions

7.2 Reporting Methods

Audience	Method	Frequency
Development Teams	Trello updates	Daily
Team Leads	Status report	Weekly
Project Manager	Risk register review	Weekly
Stakeholders	Sprint demonstrations	Bi-Weekly
Parking Operators	Progress presentation	Monthly
Management	Project dashboard/KPI report	Monthly

7.3 Communication Tools

- Trello: Backlog, sprint planning, and task tracking
- Microsoft Teams: Team communication and meetings
- Email: Formal stakeholder communication
- Sprint Reviews: Project demonstrations
- Risk Register: Risk tracking
- Status Reports: Project monitoring

8. Resource Management Plan

8.1 Project Resource Plan

Role	Name	Skill Level	FTE %	Hours
Project Manager	Sarah Johnson	Expert	20%	120
Product Owner	Michael Chen	Expert	15%	90
Business Analyst	Emma Rodriguez	Advanced	15%	90
Mobile Developer	David Kim	Advanced	50%	300
Web Developer	Olivia Parker	Advanced	50%	300

Backend Developer	James Wilson	Expert	60%	360
Mapping Developer	Ethan Martinez	Intermediate	25%	150
Payment Developer	Sophia Patel	Advanced	25%	150
QA Engineer	Isabella Garcia	Advanced	30%	180
DevOps Engineer	Alexander Brown	Advanced	20%	120

Total Planned Hours: 1,860

9. RACI Matrix

Deliverable	PM	PO	BA	Dev Team	QA	DevOps
Requirements Gathering	A	C	R	I	I	I
SRS Development	A	C	R	I	I	I
UI/UX Design	C	A	C	R	I	I
Authentication System	C	I	I	R	C	I
Parking Search & Maps	C	I	I	R	C	I
Reservations	C	I	I	R	C	I
Payment Processing	C	I	I	R	C	I
Operator Dashboard	C	I	I	R	C	I
Reporting & Analytics	C	I	I	R	C	I
System Testing	I	I	I	C	A/R	I
Deployment	I	I	I	C	C	A/R
Final Release	A	C	I	C	C	R

Legend

- R = Responsible
- A = Accountable
- C = Consulted
- I = Informed

10. Cost Management Plan

The Smart Parking Platform uses a Bottom-Up Estimation Approach because the WBS, backlog, and staffing requirements are already defined.

10.1 Labor Cost Estimate

Role	Hours	Rate	Cost
Project Manager	120	$65	$7,800
Product Owner	90	$60	$5,400
Business Analyst	90	$50	$4,500
Mobile Developer	300	$70	$21,000
Web Developer	300	$70	$21,000
Backend Developer	360	$80	$28,800
Mapping Developer	150	$65	$9,750
Payment Developer	150	$70	$10,500
QA Engineer	180	$55	$9,900
DevOps Engineer	120	$75	$9,000

Labor Subtotal: $127,650

10.2 Non-Labor Costs

Category	Cost
Cloud Hosting	$3,000
Database Services	$1,500
Development Tools & Licenses	$2,000
Mapping APIs	$2,500
Payment Gateway Testing	$1,500
Security & Compliance Tools	$2,500

Infrastructure Subtotal: $13,000

10.3 Project Budget Summary

Category	Cost
Labor	$127,650
Infrastructure & Tools	$13,000
Contingency Reserve (15%)	$21,098
Total Project Budget	$161,748

10.4 CAPEX vs OPEX

CAPEX (One-Time Costs)	OPEX (Operational Costs)
• Software Development	• Cloud Hosting
• System Design	• API Subscriptions
• Initial Deployment	• Monitoring Services
• Development Hardware	• Maintenance & Support

10.5 Monthly Cashflow

Month	Labor	Infrastructure	Contingency	Total
September	$28,000	$1,500	$4,000	$33,500
October	$35,000	$2,000	$5,000	$42,000
November	$38,000	$3,500	$6,000	$47,500
December	$26,650	$6,000	$6,098	$38,748

Total Budget: $161,748

10.6 Hidden Costs and Mitigation

Mitigation	Hidden Cost	Risk

Rate limiting and monitoring	API Usage Limits	Increased costs
Usage alerts and forecasting	Cloud Storage Growth	Budget overruns
Annual budgeting reviews	License Renewals	Unexpected expenses
Scheduled refactoring	Technical Debt	Future maintenance costs
Early compliance reviews	Security Compliance	Added development effort
Automated retention policies	Backup & Recovery	Additional storage costs

10.7 Earned Value Management (EVM)

Example Mid-Project Performance

Metric	Formula	Value
BAC	Budget at Completion	$161,748
PV	BAC × 50%	$80,874
EV	BAC × 45%	$72,786
AC	Actual Cost	$90,000
SPI	EV ÷ PV	0.90
CPI	EV ÷ AC	0.81
EAC	BAC ÷ CPI	$199,688
ETC	EAC − AC	$109,688

Interpretation

- SPI = 0.90: Project is slightly behind schedule
- CPI = 0.81: Project is currently over budget
- EAC = $199,688: Forecasted total project cost if current trends continue

11. Stakeholder Management

11.1 Stakeholder Analysis

Stakeholder	Power	Interest	Strategy
Project Manager	High	High	Manage Closely
Parking Facility Operators	High	High	Manage Closely
City Transportation Department	High	Medium	Keep Satisfied
Payment Providers	High	Medium	Keep Satisfied
Development Team	Medium	High	Keep Informed
Drivers & Vehicle Owners	Low	High	Keep Informed
General Public	Low	Low	Monitor

11.2 Power–Interest Grid

	High Interest	Low Interest
High Power	Course Instructor, Project Manager, Parking Operators	City Transportation Department, Payment Providers
Low Power	Drivers, Development Team	General Public

12. Project Charter

Item	Description
Project Name	Smart Parking Platform
Sponsor	WE ARE $oftware ¢orp.
Project Manager	Emiliano Ortiz
Business Need	Reduce parking search time and improve parking utilization
Objectives	Real-time parking search, reservations, payments, navigation, reporting
In Scope	Authentication, search, reservations, payments, notifications, analytics

Out of Scope	Parking construction, traffic system control, hardware manufacturing
Constraints	Fixed semester schedule, third-party APIs, compliance requirements
Deliverables	SRS, WBS, Backlog, Trello Board, Risk Register, Resource Plan, Final System
Success Criteria	Core functionality demonstrated and project documentation completed

13. Team Charter

13.1 Team Roles

Role	Team Member
Project Manager	Sarah Johnson
Product Owner	Michael Chen
Business Analyst	Emma Rodriguez
Mobile Developer	David Kim
Web Developer	Olivia Parker
Backend Developer	James Wilson
Mapping Developer	Ethan Martinez
Payment Developer	Sophia Patel
QA Engineer	Isabella Garcia
DevOps Engineer	Alexander Brown

13.2 Team Standards

Area	Agreement
Communication	Microsoft Teams and Trello
Meetings	Follow communication plan schedule
Task Management	Trello backlog and sprint boards

Documentation	Maintain current project documentation
Quality	Follow QA and QC procedures
Accountability	Complete assigned work on schedule

13.3 Leadership and Conflict Resolution

Topic	Approach
Leadership Style	Democratic Leadership
Decision Making	Team input with PM approval when required
Primary Conflict Strategy	Collaboration
Secondary Conflict Strategy	Compromise
Escalation Path	Project Manager
